

June 2017 Progress

Work Completed, Week Ending 6/30/17:

- Continued installing beams, girts and bracing along building perimeter.
- Continued pretension of bolts.
- Checked column plumb.
- Continued accepting deliveries of roof beams and bracing.
- Continued installing storm sewer.
- Performed grading and testing in the wash rack and apron areas.
- Undercut the elevator pit to remove sediment deposition.
- Poured piers.
- Continued installation of electrical conduit in north parking lot and along entrance road.
- Began chipping columns to investigate anchor bolts damaged by fallen columns.
- Held asphalt pre-paving meeting.
- Held concrete pre-paving meeting.

Work Completed, Week Ending 6/23/17:

- Experienced delays due to rain and lightning.
- Continued installing storm sewer between pipe.
- Pressure washed steel.
- Performed minimal grading in the wash rack and apron areas.
- Performed dewater activities.

Work Completed, Week Ending 6/16/17:

- Experienced delays due to rain and lightning.
- Continued receiving deliveries of low bay steel.
- Continued bolting high bay steel.
- Performed bolt testing.
- Continued installing storm sewer between pipe between structures.
- Electrician continued installing conduit in north parking lot and along entrance road.
- Continued grading in the wash rack and apron areas.
- Performed maintenance of silt fence.
- Continued dust control with water truck.


Work Completed, Week Ending 6/9/17:

- Continued bolting high bay steel and installing purlins and braces.
- Began receiving deliveries of low bay steel.
- Continued installing storm sewer.
- Wrecked forms, backfilled and compacted around footers in the administrative building area.
- Electrician continued installing conduit in north parking lot and along entrance road.
- Performed grading in the apron area.
- Performed maintenance of silt fence.
- Continued dust control with water truck.

Work Completed, Week Ending 6/2/17:

- Continued bolting high bay steel and installing purlins.
- Poured remaining interior spread footings, except for elevator pit.
- Continued backfilling around apron storm structures and pipes.
- Continued installing storm pipe.
- Electrician continued installing conduit.
- Performed maintenance of silt fence.
- Continued dust control with water truck.



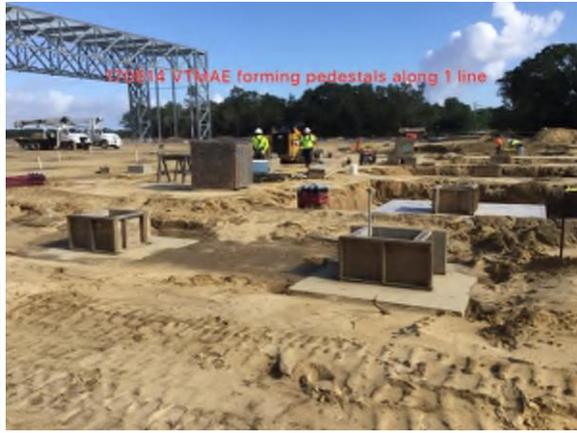



170623 VTMAE erecting columns



170627 VTMAE storm pipe being installed between S-420 & S-430



170627 VTMAE steel erection continuing



170628 VTMAE plumb testing for columns



170628 VTMAE roof framing



170629 VTMAE steel erection continuing
